


THRALL ISD

ELEMENTARY SCHOOL

CONSTRUCTION UPDATE

- METER INSTALLATION IS COMPLETE.
- LIFT STATION AND GENERATOR INSTALLATIONS ARE COMPLETE.
- BRICK WORK IS NEARING COMPLETION.
- ROOF WORK IS IN PROGRESS.
- EIFS ARE IN PROGRESS.
- WING A CEILING GRID AND LIGHTING INSTALLATIONS ARE IN PROGRESS.
- WING B AND C SHEETROCK INSTALLATIONS ARE IN PROGRESS.

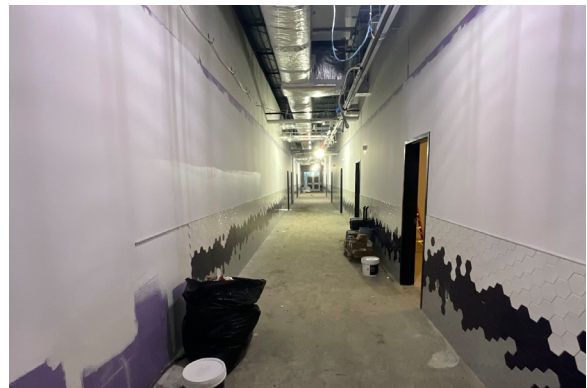

COST SUMMARY

Construction Contingency Balance:	\$749,048
Owner Contingency Balance:	\$687,974
Total Budget:	\$38,027,876
Total Completed & Stored To Date:	\$20,560,782
Percentage Complete:	54%



DIFFERENT FROM THE GROUND UP



GALLAGHER
A CUMMING GROUP COMPANY
