

THRALL ISD

ELEMENTARY SCHOOL

CONSTRUCTION UPDATE

- SEQUENCE ONE STEEL ERECTIONS ARE IN PROGRESS.
- DECK AND JOIST INSTALLATIONS ARE SCHEDULED TO BEGIN SOON.



COST SUMMARY

Construction Contingency Balance:	\$1,183,426
Owner Contingency Balance:	\$700,000
Total Budget:	\$38,092,458
Total Completed & Stored To Date:	\$9,818,567
Percentage Complete:	26%



DIFFERENT FROM THE GROUND UP



GALLAGHER
A CUMMING GROUP COMPANY

THRALL ISD

HIGH SCHOOL


CONSTRUCTION UPDATE

- NORTH STORM DRAIN INSTALLATIONS ARE COMPLETE.
- HIGH SCHOOL TO CTE BUILDING FENCE/GATE INSTALLATION IS COMPLETE.
- MECHANICAL, ELECTRICAL, AND PLUMBING ROUGH-INS ARE NEARING COMPLETION.
- NORTH SITE UTILITY INSTALLATIONS ARE NEARING COMPLETION.
- EARTHWORK IS IN PROGRESS.
- FRAMING AND SHEETING INSTALLATIONS ARE IN PROGRESS.



COST SUMMARY

Construction Contingency Balance:	\$678,427
Owner Contingency Balance:	\$300,000
Total Budget:	\$11,745,461
Total Completed & Stored To Date:	\$3,128,630
Percentage Complete:	27%

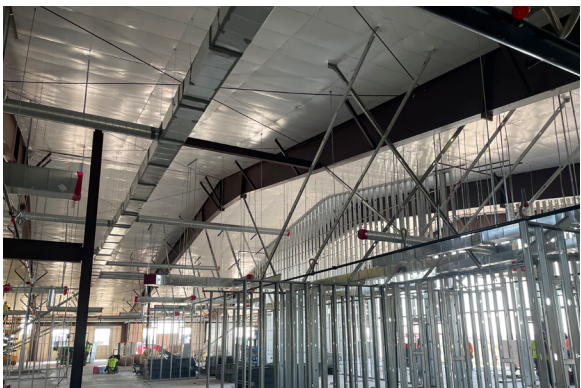

DIFFERENT FROM THE GROUND UP



GALLAGHER
A CUMMING GROUP COMPANY
