

THRALL ISD

ELEMENTARY SCHOOL


CONSTRUCTION UPDATE

- WING A, CORE, AND WING B FIRST FLOOR FRAMING INSTALLATIONS ARE COMPLETE.
- WING C, SECOND FLOOR, CONCRETE POURS ARE IN PROGRESS.
- WING D STEEL ERECTION IS IN PROGRESS.
- WING C FRAMING IS IN PROGRESS.
- WINDOW INSTALLATIONS ARE IN PROGRESS.
- MASONRY WORK IS IN PROGRESS.



COST SUMMARY

Construction Contingency Balance:	\$792,174
Owner Contingency Balance:	\$687,974
Total Budget:	\$38,027,876
Total Completed & Stored To Date:	\$16,963,719
Percentage Complete:	45%

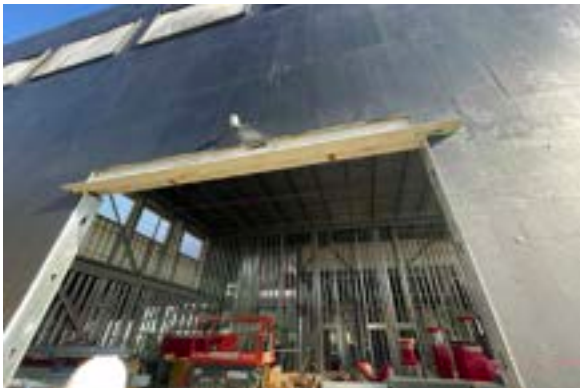

DIFFERENT FROM THE GROUND UP



GALLAGHER
A CUMMING GROUP COMPANY

THRALL ISD

HIGH SCHOOL

CONSTRUCTION UPDATE

- EXTERIOR SIDEWALK WORK IS NEARING COMPLETION.
- TOUCH-UPS AND FINAL CLEAR ARE IN PROGRESS.
- PUNCH-LIST ITEM CORRECTIONS ARE SCHEDULED TO BEGIN SOON.



COST SUMMARY

Construction Contingency Balance:	\$584,075
Owner Contingency Balance:	\$249,337
Total Budget:	\$11,745,461
Total Completed & Stored To Date:	\$6,773,277
Percentage Complete:	58%



DIFFERENT FROM THE GROUND UP



GALLAGHER
A CUMMING GROUP COMPANY
