

THRALL ISD

ELEMENTARY SCHOOL

CONSTRUCTION UPDATE

- AREAS B, C, AND D EXTERIOR FRAMING IS NEARING COMPLETION.
- INTERIOR FRAMING IS IN PROGRESS.
- DENS GLASS SHEATHING IS IN PROGRESS.



COST SUMMARY

Construction Contingency Balance:	\$1,130,445
Owner Contingency Balance:	\$687,974
Total Budget:	\$38,027,876
Total Completed & Stored To Date:	\$12,601,677
Percentage Complete:	33%



DIFFERENT FROM THE GROUND UP



GALLAGHER
A CUMMING GROUP COMPANY

THRALL ISD

HIGH SCHOOL


CONSTRUCTION UPDATE

- MECHANICAL, ELECTRICAL, AND PLUMBING WORK IS COMPLETE.
- FRAMING IS COMPLETE.
- NORTH PARKING LOT SIDEWALK WORK IS NEARING COMPLETION.
- PARKING LOT BASE WORK IS NEARING COMPLETION.
- EXTERIOR MASONRY BRICK WORK IS NEARING COMPLETION.



COST SUMMARY

Construction Contingency Balance:	\$550,472
Owner Contingency Balance:	\$257,537
Total Budget:	\$11,745,461
Total Completed & Stored To Date:	\$4,893,184
Percentage Complete:	42%

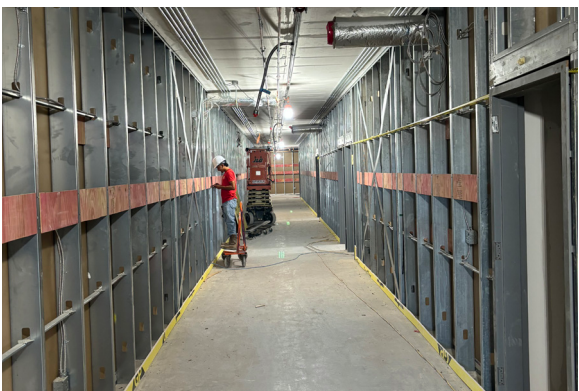

DIFFERENT FROM THE GROUND UP



GALLAGHER
A CUMMING GROUP COMPANY
